

Project Planning Phase

Project Planning Template (Product Backlog, Sprint Planning, Stories, Story points)

Date	01 October 2026
Team ID	SWTID-2026-2615
Project Name	Implement Client Script & UI Policy (Incident)
Maximum Marks	5 Marks

Product Backlog, Sprint Schedule, and Estimation (4 Marks)

Product backlog and sprint schedule for the ServiceNow Administrator project "Implement Client Script & UI Policy (Incident)".

Sprint	Functional Requirement (Epic)	User Story Number	User Story / Task	Story Points	Priority	Team Members
Sprint-1	Setup & Requirement Analysis	USN-1	As an admin, I can set up the ServiceNow Personal Developer Instance (PDI) and log in to access the Incident module.	2	High	Sanjana sree M
Sprint-1		USN-2	As an admin, I can create an Update Set (Incident_ClientScript_UIPolicy) to capture all customizations.	1	High	SRI SADHA S
Sprint-1		USN-3	As an admin, I can analyze the Incident form and identify the fields that need validation and dynamic behavior.	3	High	Mrinalini Baranidharan
Sprint-1		USN-4	As an admin, I can configure the Incident form layout and fields required for the use case.	2	Medium	Sanjana sree M
Sprint-2	UI Policy Implementation	USN-5	As an admin, I can create a UI Policy that makes Short description mandatory when State is New.	3	High	SRI SADHA S
Sprint-2		USN-6	As an admin, I can create a UI Policy that makes Resolution code and Resolution notes mandatory when State is Resolved.	3	High	Mrinalini Baranidharan
Sprint-2		USN-7	As an admin, I can create a UI Policy that keeps Assigned to read-only until Assignment group is selected.	2	Medium	Sanjana sree M
Sprint-2		USN-8	As an admin, I can configure UI Policy conditions, UI Policy Actions and the 'Reverse if false' and 'On load' options.	2	Medium	SRI SADHA S
Sprint-3	Client Script Implementation	USN-9	As an admin, I can create an onChange Client Script on Category that clears Subcategory and shows an information message.	3	High	Mrinalini Baranidharan
Sprint-3		USN-10	As an admin, I can create an onChange Client Script on Priority that shows a warning when Priority is 1 - Critical.	3	Medium	Sanjana sree M
Sprint-3		USN-11	As an admin, I can create an onLoad Client Script that shows a message and sets default values on a new Incident form.	2	Medium	SRI SADHA S
Sprint-3		USN-12	As an admin, I can create an onSubmit Client Script that validates Short description length and stops submission with an error message.	5	High	Mrinalini Baranidharan

Sprint	Functional Requirement (Epic)	User Story Number	User Story / Task	Story Points	Priority	Team Members
Sprint-4	Testing & Documentation	USN-13	As a tester, I can verify all UI Policies with positive and negative test cases on the Incident form.	3	High	Sanjana sree M
Sprint-4		USN-14	As a tester, I can verify the onLoad, onChange and onSubmit Client Scripts on the Incident form.	3	High	SRI SADHA S
Sprint-4		USN-15	As a team, we prepare the documentation, screenshots and project report.	2	Medium	Mrinalini Baranidharan
Sprint-4		USN-16	As an admin, I can finalize the Update Set and complete the final review and demo.	1	Medium	Sanjana sree M

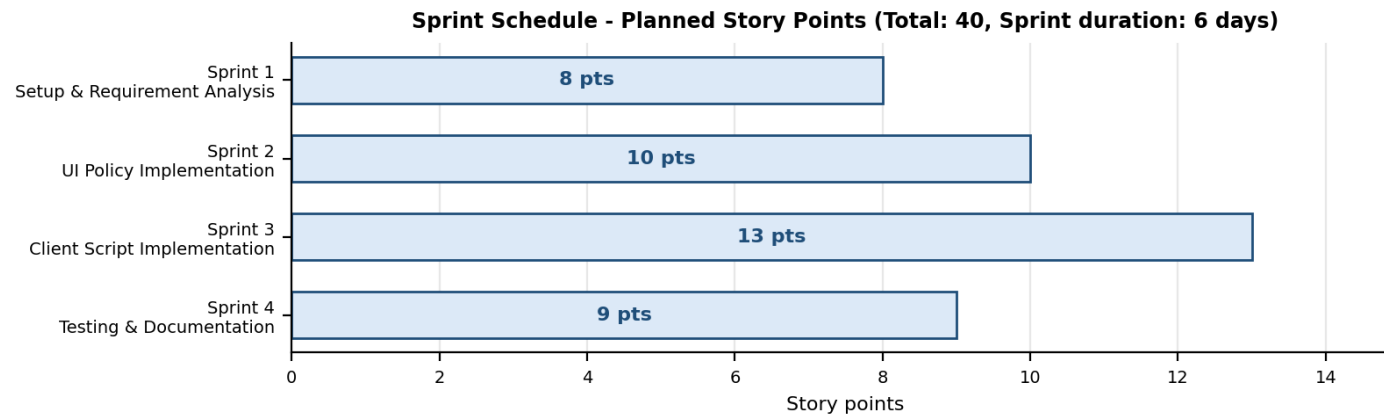


Figure 1: Sprint schedule and story-point representation.

Planning Logic

Sprint	A fixed period in which the team completes a set of tasks. Sprint duration = 6 days.
Epic	A big task that is broken into smaller stories: Setup & Analysis, UI Policy, Client Script, Testing & Documentation.
Story (USN)	A small task that belongs to an Epic. This project has 16 user stories (USN-1 to USN-16).
Story Point	Effort needed for a story, using the scale 1, 2, 3, 5: 1 = Very Easy, 2 = Normal, 3 = Moderate, 5 = Difficult.
Sprint totals	Sprint-1 = 2+1+3+2 = 8; Sprint-2 = 3+3+2+2 = 10; Sprint-3 = 3+3+2+5 = 13; Sprint-4 = 3+3+2+1 = 9. Total = 8+10+13+9 = 40 story points.
Velocity	Velocity = Total Story Points Completed / Number of Sprints = 40 / 4 = 10 story points per sprint.

Project Tracker, Velocity & Burndown Chart: (4 Marks)

Sprint	Total Story Points	Duration	Sprint Start Date	Sprint End Date (Planned)	Story Points Completed (as on Planned End Date)	Sprint Release Date (Actual)
Sprint-1	8	6 Days	05 Sep 2026	10 Sep 2026	8	10 Sep 2026
Sprint-2	10	6 Days	12 Sep 2026	17 Sep 2026	10	17 Sep 2026
Sprint-3	13	6 Days	19 Sep 2026	24 Sep 2026	13	24 Sep 2026
Sprint-4	9	6 Days	26 Sep 2026	01 Oct 2026	9	01 Oct 2026
Total	40	24 Days			40	

Work Item Tracker

Work Item	Status	Validation
ServiceNow PDI and Incident module access	Completed	PDI active; admin login successful; Incident module opens.
Update Set	Completed	Update Set Incident_ClientScript_UIPolicy created and set as current.
Incident form analysis and layout	Completed	Fields identified and form layout configured.
UI Policy - Short description mandatory	Completed	Short description is mandatory when State is New.
UI Policy - Resolution fields mandatory	Completed	Resolution code and Resolution notes mandatory when State is Resolved.
UI Policy - Assigned to read-only	Completed	Assigned to is read-only until Assignment group is selected.
Client Script - onLoad	Completed	Message displayed and defaults set on a new Incident form.
Client Script - onChange (Category)	Completed	Subcategory cleared and message shown when Category changes.
Client Script - onChange (Priority)	Completed	Warning shown when Priority is 1 - Critical.
Client Script - onSubmit	Completed	Submission blocked with error message when Short description is too short.
Testing	Completed	UI Policies and Client Scripts validated with positive and negative cases.
Documentation and Update Set	Completed	Report, screenshots prepared; Update Set finalized.

Velocity:

Sprint duration = 6 days and total story points = 40 over 4 sprints, so the team's velocity is $40 / 4 = 10$ story points per sprint.

Average Velocity (AV) per iteration unit (story points per day) = $\text{Velocity} / \text{Sprint duration} = 10 / 6 = 1.67$ story points per day.

Burndown Chart:

A burn down chart is a graphical representation of work left to do versus time. The chart below shows remaining story points (out of 40) at the end of each sprint against the ideal burndown line.

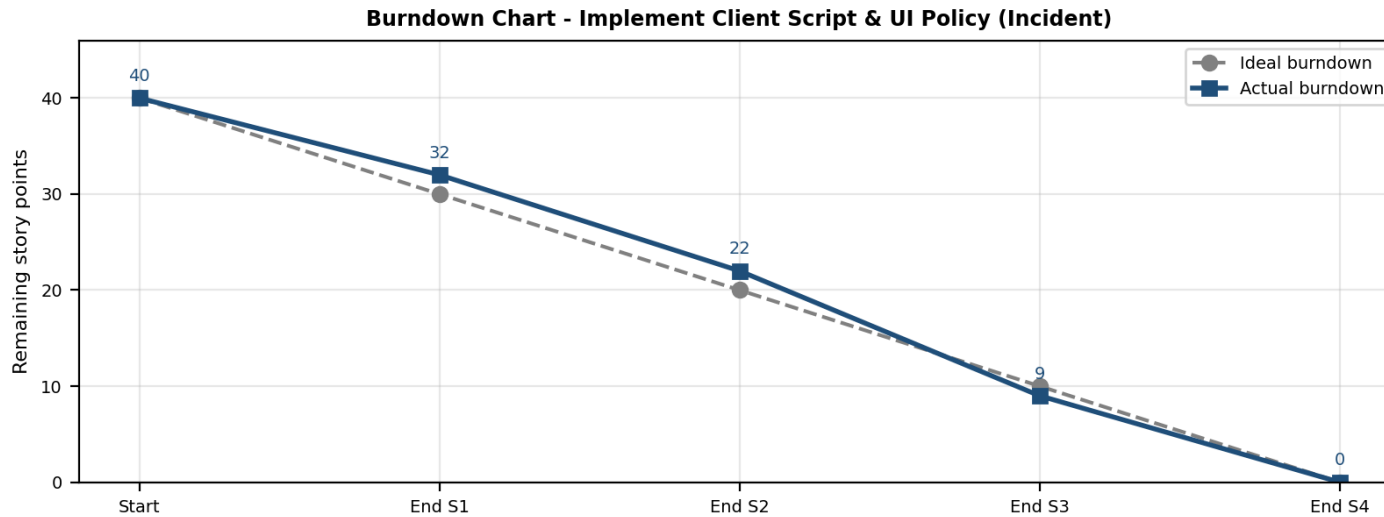


Figure 2: Burndown chart for the project.

<https://www.visual-paradigm.com/scrum/scrum-burndown-chart/>

<https://www.atlassian.com/agile/tutorials/burndown-charts>

Reference:

<https://www.atlassian.com/agile/project-management>

<https://www.atlassian.com/agile/tutorials/how-to-do-scrum-with-jira-software>
